

BANGLADESH WATER DEVELOPMENT
BOARD



Project Completion Report : IMED-04/2003(Revised)
Project period : May, 2016 to June, 2018

Name of the Project : Temporary Bank Protective Work along
the Left Bank of The Padma River at West Narisha Bazar &
Meghula Bazar at Dohar Upazila in Dhaka District (1st Revised)

NAME OF DIVISION : DHAKA O&M DIVISION-II, BWDB, DHAKA.

NAME OF CIRCLE : DHAKA O&M CIRCLE, BWDB, DHAKA.

NAME OF ZONE : CENTRAL ZONE, BWDB, DHAKA.

Government of the People's Republic of Bangladesh
Ministry of Planning

Implementation Monitoring and Evaluation Division

PROJECT COMPLETION REPORT : IMED 04/2003 (Revised)

A. PROJECT DESCRIPTION :

01. Name of the Project : Temporary Bank Protective Work along the Left Bank of The Padma River at West Narisha Bazar & Meghula Bazar at Dohar Upazila in Dhaka District (1st Revised)

02. Administrative Ministry/Division : Ministry of Water Resources

03. Executing Agency : Bangladesh Water Development Board

04. Location of the Project : Upazila :Dohar, District: Dhaka.

05. Objective of the Project

- To arrest river bank erosion and flood protective coverage by construction of river bank protective works.
- To temporary protect the Dohar Upazila area from the erosion of Padma River. Also to protect different physical infrastructure such as government & primary school, high school, college, madrasa, mosque, homestead, market, fishery and poultry firms, cultivable land, bridge, previous protective works and other private & public properties.

06. Estimated Cost

:

(In lakh Taka)

	Original	Latest Revised
(a) Total	1689.38	1934.78
(b) Taka	1689.38	1934.78
(c) Foreign Currency	-	-
(d) Project Aid	-	-
(e) RPA	-	-



07.	Date of Approval	:	PCP	PP
(a)	Original	:	-	31.05.16
(b)	Latest Revised	:	-	24.04.17

08. Implementation Period

	Date of Commencement	Date of Completion
(a) Original	May, 2016	June, 2017
(b) Latest Revised	May, 2016	June, 2018
(c) Actual	May, 2016	June, 2018

09. Financing Arrangement (Source-wise) :

9.1 Status of Loan/Grant

a) Foreign Financing : Not Applicable

Source (s)	Currency as per Agreement	Amount in US \$ (Million)	Nature (Loan/Grant/supplier's/credit)	Date of Agreement	Date of Effective -ness	Date of Closing	
						Original	Revised
1	2	3	4	5	6	7	8

b) GOB :

(In lakh Taka)			
Total amount	Loan	Grant	Cash Foreign Exchange
1	2	3	4
1934.78	-	1934.78	-

9.2 Utilization of Project Aid : (Source wise) Not Applicable

Source (s)	Total Amount		Actual Expenditure		Unutilized Amount	
	In US \$	In Local Currency	In US \$	In Local Currency	In US \$	In Local Currency
	2	3	4	5	6	7

9.3 Re-imbursible Project Aid (RPA): Not Applicable

R P A Amount		Amount Spent	Amount Claimed	Amount Re-imbursed	Remarks
As per PP	As per Agreement				
1	2	3	4	5	6

B. IMPLEMENTATION POSITION

01. Implementation Period :

Implementation Period as per DPP		Actual Implementation period	Time Over-run (% of original implementation period)	Remarks
Original	Latest Revised			
1	2	3	4	5
May, 2016 to June, 2017	May, 2016 to June, 2018	May, 2016 to June, 2018	85.71%	Due to increased scope of work according to RDPP

02. Cost of the Project :

(In lakh Taka)

Description	Estimated Cost		Actual expenditure	Cost over-run (% of original cost)	Remarks
	Original	Latest revised			
1	2	3	4	5	6
TOTAL	1689.38	1934.78	1729.22	2.36%	-
TAKA	1689.38	1934.78	1729.22	2.36%	-
PA	-	-	-	-	-

03. Project Personnel : . Project work has been completed by existing manpower of BWDB.

Sanctioned strength as per PP	Manpower employed during execution	Status of the existing manpower			Manpower Employed	
		Manpower requirement for O&M as per pp	Existing manpower for O & M	Others		
1	2	3	4	5	Male	Female
Officer (s)	-	-	-	-	-	-
Staff(s)	-	-	-	-	-	-
Total :	-	-	-	-	-	-

04. Training of Project Personnel (Foreign/Local) : Not Applicable

Field of Training /Study tour/workshop/ Seminar etc.	Provision as per DPP		Actual		Remarks
	Number of person	Man - months	Number of person	Man - months	
1	2	3	4	5	6

a. Foreign

b. Local

✍

05. Component-wise Progress (As per latest approved DPP) :

(In lakh Taka)

Items of work (as per PP)	Unit	Target (as per DPP)		Actual Progress		Reasons for deviation (±)
		Financial	Physical (Quantity)	Financial	Physical (Quantity)	
1	2	3	4	5	6	7
(a) Revenue Component:						
Fuel & Gas - 1 Item.	1 item	2.00	100%	2.00	100%	
Petrol & Lubricant	1 item	2.00	100%	2.00	100%	
Stationery, seal & stamps	1 item	1.00	100%	1.00	100%	
Printing & Publications	1 item	1.00	100%	1.00	100%	
Honorarium/ Fee/ Remuneration for different committee(PSC, TEC, PIC etc.),	1 item	2.00	100%	2.00	100%	
Survey & Investigation -1 Item	1 item	5.00	100%	5.00	100%	
Repairs, maintenance & rehabilitation						
Repair & Maintenance of existing vehicles	1 item	2.00	100%	2.00	100%	
Sub-Total (a):		15.00		15.00	100%	
(b) Capital Component						
Temporary Bank Protective work	M	1549.19	2375m	1480.19	2375m	
Dredging work of Padma river	Km. (Cum)	370.59	1.821Km (2.85 Lakh Cum)	234.03	1.821 Lakh Cum	Scope of dredging reduced due to morphological change of river course.
Sub-Total (b):		1919.78	100%	1714.22	100%	
Physical Contingency (c)	1 item	0.00	0.00%	0.00	0.00%	
Price Contingency (d)	1 item	0.00	0.00%	0.00	0.00%	
Grand Total (a+b+c+d):		1934.78	100%	1729.22	100%	



06. Information regarding Project Director (s) :

Name & Designation with pay Scale.	Full time	Part time	Responsible for more than one project	Date of		Remarks
				Joining	Transfer	
1	2	3	4	5	6	7
Md. Abdul Matin Sarkar Superintending Engineer Dhaka O&M Circle BWDB,Dhaka.	Full time	-	Yes	19.07.16	-	

07. Procurement of Transport (in Nos.) : No Provision of vehicle Procurement of the project.

Type of transport	Number as per P.P.	Procured with date	Transferred to Transport Pool with date	Transferr ed to O & M with date	Condemned/ damaged with date	Remarks
1	2	3	4	5	6	7
Car						
Jeep						
Microbus						
Minibus						
Bus						
Pick-up						
Truck						
Motor Cycle						
By-cycle						
Speed Boat						
Launch						
Others with name						

Handwritten signature/initials

08. Procurement of Goods, Works and Consultancy Services:

08.1 Goods & Works of the Project costing above Tk. 200.00 lakh. and Consultancy above Tk. 100.00 lakh :

Description of procurement (goods/works /consultancy) as per bid document	Tender/Bid/Proposal Cost (in crore Taka)		Tender/Bid/Proposal		Date of completion of works/services and supply of goods	
	As per DPP	Contracted value	Invitation date	Contract signing/ L.C opening date	As per contract	Actual
1	2	3	4	5	6	7
Temporary Bank protective work using Sand Filed, Geo Bag & Gunny Bag dumping Km. 3.487 to km. 3.887 = 400.00m	2.76	2.35	16.06.16	16.08.16	15.01.17	31.05.17
Temporary Bank protective work using Sand Filed, Geo Bag & Gunny Bag dumping Km. 3.887 to km. 4.287 = 400.00m	2.76	2.35	13.06.16	16.08.16	15.01.17	31.05.17
Temporary Bank protective work using Sand Filed, Geo Bag & Gunny Bag dumping Km. 4.287 to km. 4.687 = 400.00m	2.76	2.59	13.06.16	10.08.16	08.01.17	31.05.17
Temporary Bank protective work using Sand Filed, Geo Bag & Gunny Bag dumping Km. 2.312 to km. 2.562 = 250.00m	1.73	1.55	13.06.16	16.08.16	15.01.17	31.05.17
Temporary Bank protective work using Sand Filed, Geo Bag & Gunny Bag dumping Km. 2.562 to km. 2.812 = 250.00m	1.73	1.55	01.08.16	27.09.16	23.02.17	31.05.17
Temporary Bank protective work using Sand Filed, Geo Bag & Gunny Bag dumping Km. 2.812 to km. 3.487 = 675.00m	5.95	5.95	29.03.17	30.04.17	30.06.17	21.05.18
River Dredging work by dredger from km. 2.812 to km. 4.633 = 1.821km.	4.99	4.99	31.07.16	31.07.16	30.06.17	30.06.17

A.

8.2 Use of Project Consultant (s) (Foreign/Local): Not Applicable

Name of the Field	Approved man month		Actual man month utilised	Remarks
	As per PP	As per contract		
1	2	3	4	5

a) Foreign :

b) Local :

09. Construction/Erection/Installation Tools & Equipment : Not Applicable

Description of items	Quantity (as per PP)	Quantity procured with date	Transferred to O & M with date	Disposed off as per rule with date	Balance	Remarks
1	2	3	4	5	6	7

C. FINANCIAL AND PHYSICAL PROGRAMME :

01. (a) Original and revised schedule as per DPP :

(In lakh Taka)

Financial Year	Financial provision & physical target as per original DPP				Financial provision & physical target as per latest revised DPP			
	Total	Taka	P.A.	Physical %	Total	Taka	P.A.	Physical %
1	2	3	4	5	6	7	8	9
2015-16	479.82	479.82	-	28.40%	0.00	0.00	-	0.00%
2016-17	1209.56	1209.56	-	71.60%	1834.78	1834.78	-	94.83%
2017-18	0.00	0.00	-	0.00%	100.00	100.00	-	5.17%
Total	1689.38	1689.38	-	100%	1934.78	1934.78	-	100%

01. (b) Revised ADP allocation and progress :

(In lakh Taka)

Financial Year	Revised Allocation & target				Taka release	Expenditure & physical progress			
	Total	Taka	P.A.	Physical %		Total	Taka	P.A.	Physical %
1	2	3	4	5	6	7	8	9	10
2015-16	0.00	0.00	-	0.00%	-	-	-	-	-
2016-17	1834.78	1834.78	-	90.00%	1670.00	1483.22	1483.22	-	90.00%
2017-18	100.00	100.00	-	10.00%	250.00	246.00	246.00	-	10.00%
Total	1934.78	1934.78	-	100%	1920.00	1729.22	1729.22	-	100%

D. ACHIEVEMENT OF OBJECTIVES OF THE PROJECT :

Objectives as per PP	Actual achievement	Reasons for shortfall, if any
(a) To arrest river bank erosion and flood protective coverage by construction of river bank protective works.	River bank erosion are reduce by temporary bank protective works.	No shortfall
(b) Enhanced dry season flow and quick drainage	dry season flow and quick drainage are Enhanced	
(c) Improved navigation and water quality	Navigation and water quality are Improved.	
(d) Environmental improvement achieved	Achieved.	
(e) Accelerated Macro-economic activities	Accelerated Macro-economic activities are Improved.	

E. BENEFIT ANALYSIS

01. Annual Out-put :

Items of out-put	Unit	Estimated quantity expected at full capacity	actual quantity of out-put during the 1st year of operation at full capacity (or during, real production for newly completed project).
It is a project consists of only Two physical component like Temporary river bank protective work and Dredging work. Its direct benefit cannot be quantifiable. Valuable immovable properties (both public & private properties) within the project area has been saved by virtue of implementation of the Project. Safeguard of human life and social and natural security for sustainable socio-economic enhancement has also been achieved from continued threat of river bank erosion. Moreover existing flood control embankment as well as main road communication system of the project area has been saved from the erosion of the Padma River.			

02. Cost / Benefit :

Item	Estimated	Actual
(1) Benefit cost ratio of the project		Will be evaluated later by concerned directorate of BWDB IMED.
(i) Financial	2.65 : 1.00	
(ii) Economic	3.10 : 1.00	
(2) Internal Rate of Return		
(i) Financial	51.61%	
(ii) Economic	61.46%	

02. Please give reasons for shortfall, if any, between the estimated and actual benefit :
Not Applicable

F. MONITORING AND AUDITING

0.1 Monitoring:

Name & designation of the inspecting official	Date of Inspection	Identified Problems	Recommendations
1	2	3	4
মোঃ মাহফুজুর রহমান অতিঃ মহাপরিচালক (পরিকল্পনা), বাংলাদেশ পানি উন্নয়ন বোর্ড।	18.12.16	No Problems Found	-
আবুল কালাম আজাদ প্রধান প্রকৌশলী, কেন্দ্রীয় অঞ্চল বাপাউবো, ঢাকা।	18.12.16	No Problems Found	-
মোঃ আব্দুল মতিন সরকার প্রকল্প পরিচালক। ও তত্ত্বাবধায়ক প্রকৌশলী, ঢাকা পওর সার্কেল বাপাউবো, ঢাকা।	18.12.16 08.02.17 18.03.17 04.04.18 30.04.18 19.04.18 24.05.18	No Problems Found	-
মোঃ জাহাঙ্গীর কবির মহাপরিচালক বাংলাদেশ পানি উন্নয়ন বোর্ড।	22.03.17	No Problems Found	-
এ এইচ এম ফখরুল ইসলাম প্রধান প্রকৌশলী, কেন্দ্রীয় অঞ্চল বাপাউবো, ঢাকা।	22.03.17 19.04.18	No Problems Found	-
কাজী তোফায়েল হোসেন তত্ত্বাবধায়ক প্রকৌশলী, ডিজাইন সার্কেল-২ বাপাউবো, ঢাকা।	18.04.17	No Problems Found	-
ফজলুর রশিদ পরিচালক পরিকল্পনা-১, বাপাউবো, ঢাকা।	04.04.18	No Problems Found	-
মোঃ মাহফুজুর রহমান মহাপরিচালক বাংলাদেশ পানি উন্নয়ন বোর্ড।	19.04.18	No Problems Found	-
কে এম আনোয়ার হোসেন অতিঃ মহাপরিচালক (পূর্ব রিজিয়ন), বাংলাদেশ পানি উন্নয়ন বোর্ড।	19.04.18	No Problems Found	-
মোঃ মোতাহার হোসেন প্রধান প্রকৌশলী, নকশা বাপাউবো, ঢাকা।	19.04.18	No Problems Found	-

(a) Ministry / Agency:

Name & designation of the inspecting official	Date of Inspection	Identified Problems	Recommendations
1	2	3	4
মন্টু কুমার বিশ্বাস যুগ্ম প্রধান পানি সম্পদ মন্ত্রণালয়।	18.03.17 19.04.18	No Problems Found	-

(b) IMED :

Name & designation of the inspecting official	Date of Inspection	Identified Problems	Recommendations
1	2	3	4
জনাব পরিমল চন্দ্র পরিচালক(উপ-সচিব) বাস্তবায়ন পরিবিধ্বন ও মূল্যায়ন বিভাগ(আইএমইডি)।	08.02.17	No Problems Found	-
জনাব লসমী চাকমা সহকারী পরিচালক বাস্তবায়ন পরিবিধ্বন ও মূল্যায়ন বিভাগ(আইএমইডি)।	30.04.17	No Problems Found	-
জনাব আফজাল হোসেন পরিচালক(উপ-সচিব) বাস্তবায়ন পরিবিধ্বন ও মূল্যায়ন বিভাগ(আইএমইডি)।	24.05.18	No Problems Found	-

Observation and Recommendations of IMED attached.(Annexure-1)

(c) Others: (Please specify)



(d) 0.2. Auditing during and after Implementation:

2.1. Internal Audit: No internal audit has been conducted.

Period of Audit	Date of submission of Audit Report	Major findings/ objections	Whether objections resolved or not.
1	2	3	4
-	-	-	-

2.2. External Audit:

Audit period	Date of submission of Audit Report	Major findings/ objections	Whether objections resolved or not.
1	2	3	4
2016-17	-	No Objections	-

G. DESCRIPTIVE REPORT

1. General Observations/Remarks of the Project on :

1.1 Background: To temporary protect the Dohar Upazila area from the erosion of Padma River. Also to protect different physical infrastructure such as government & primary school, high school, college, madrasa, mosque, homestead, market, fishery and poultry farms, cultivable land, bridge, previous protective works and other private & public properties.

1.2 Justification/Adequacy:

- River erosion mitigated
- Ensured Drainage improvement and educate draft for navigation
- Irrigation and fisheries developed
- Public & Private properties and Natural Resources protected
- Sustainable socio-economic & tertiary sector's enhancement

1.3 Objectives:

- Safety of lives, properties from river erosion
- Enhanced dry season flow and quick drainage
- Improved navigation and water quality
- Environmental improvement achieved
- Accelerated Macro-economic activities

1.4 Project revision with reasons:



In the Original approved DPP, the provision of temporary protective work were 500.00 m (km. 2.312 to Km. 2.812) at Meghula Bazar & 1200.00 m (Km. 3.487 to Km. 4.687) at Narisha Bazar Total = 1700.00 m to protect the said area only was a gap between the two Bazar of 675.00 m length. In the monsoon of 2016 the river morphology of the area changed and severe bank erosion occurred in the whole length of 1700.00 + 675.00 m = 2375 m (Km. 2.312 to Km. 4.687). The local peoples representatives of including political personnels demanded to protect the vulnerable length of 2375 m. The temporary protective work of DPP length 1700.00 m had been targeted to be completed within April/2017. It was seen that there is a gap of 675m.length downstream of Narisha Bazar, Which were not included in the program. That portion of river bank was very much threatnd. IMED representative visited the project area and suggested to take initiative for implementation of the remaining unprotected 675 m. The Director General, Bangladesh Water Development Board and Joint Chief, Ministry of Water Recourse have been visited the Project area and instructed to prepare revised DPP to include the 675 m length and complete the total length of 2375 m before upcoming monsoon to protect the on going work and vulnerable infrastructure from erosion of Padma river.

2. Rationale of the project in respect of Concept, Design, Location and Timing :

Due to immersee persistent public demand, the project DPP had been prepared for over a night. Approved of this DPP didnt require any appraisal on PEC meeting in planning Commission. The project was taken to arrest bank erosion immedately for the time being. Thats why provision of terporary protective work had been included in the DPP. Typical desin temporary protective work near by area that reach was considered. Per meter wst for that temporary protective work was 62000 th only. Giver the impotence of protected area, the project seem a cust effective temporary solution. The project has ameted bank erosion for the time being. But erosion of upstream, downstream & within the implemented reach of the project has left BWDB to take a near project for permanent bank protection.

3. Brief description on planning and financing of the project and its applicability: Not Applicable

- ♦ **Project Identification :** The project was initially Identified by local politicians, local elites etc. Those stakeholders earnestly requested the honorable private sector development affairs adviser to Honorable Prime Minister Mr. Salman F Rahman for addressing the problem of river erosion mitigation measure at Narisha Bazar. According to public demand he adviced BWDB To take this project.
- ♦ **Project Preparation :** The site was visited by the honorable private sector development affairs adviser Mr. Salman F Rahman and local politicians, local elites etc with BWDB On the basis of There Pressure the project was prepared.
- ♦ **Appraisal:** Hon'ble Planning Minister approved the project on 01 June 2016 by the Honorable Minister of Planing .



- ◆ **Credit Negotiation:** Not applicable
- ◆ **Credit Agreement :** Not applicable
- ◆ **Credit Effectiveness :** Not applicable
- ◆ **Loan Disbursement :** Not applicable
- ◆ **Loan Conditionalities :** Not applicable
- ◆ **Project Approval:** The project was approved on 01-06-2016 by the Honorable Minister of Planning .
- ◆
- ◆ **Others (if any) :** Nil.

4. Analysis of the Post-Implementation situation and result of the project :

- 4.1 Whether the beneficiaries of the project have clear knowledge about the Target/ Objectives of the project : Yes**
- 4.2 Programme for use of created-facilities of the project :** The stakeholders are directly taking advantages of the created facilities of the project.
- 4.3 O & M programme of the project : No**
- 4.4 Impact of the project -**
 - 4.4.1 Direct :**
 - a. Protection of Narisha Union Porishod office ,School, Community Hall, etc there are other govt. and non-govt properties located at Fouzdari Mour, the most densely populated area of Dohar town saved from river erosion.
 - b. Safety of public and government owned assets and natural resources of the project area.
 - 4.4.2 Indirect :**
 - a. Environmental enhancement from river erosion hazards
 - b. Sustainable socio-economic enhancement.
- 4.5 Transfer of Technology and Institutional Building through the project : Positive Impact**
- 4.6 Employment generation through the project. :** Employment generation for skilled/unskilled during construction period is more than 1 lakh man-days
- 4.7 Possibility of Self employment :** There are possibilities of self-employment as existing commercial and business centers protected from river bank erosion.
- 4.8 Possibility of women-employment opportunity :** Yes, there is possibility of women-employment through the project.
- 4.9 Women's participation in development : Yes**
- 4.10 Probable Impact on Socio-Economic activity :** Protecting the river bank erosion, various infrastructures are saved from the erosion. The impact of socio-economic is balanced in the locality.
- 4.11 Impact on environment :** Positive Impact: Environmental enhancement is achieved through the implementation of the project. Bank erosion hazards of environment are eradicated.
- 4.12 Sustainability of the project :** The project was taken to avert river erosion temporary basis that it has fulfilled for sustainability as river banks on that reach a new project has been taken for permanent bank protection.
- 4.13 Contribution to poverty alleviation/reduction :** The project fulfilled the following benefits in compatible strategic goal (i. e. a) reduction of vulnerability to water related disaster.

12

- 4.14 **Opinion of the public representatives, local elite, local administration, teachers, religious leaders, women's representatives etc :** Positive remarks regarding the project.
- 4.15 **Contribution of Micro-credit programmes and Comments on overlapping with any NGO activities :** Not Applicable

5. Problems encountered during Implementation (with duration & steps taken to remove those)


5.1	Project Management : N/A	5.12	Project aid disbursement and re-imbursment : N/A
5.2	Project Director : N/A		
5.3	Land Acquisition : N/A	5.13	Mission of the development partners : N/A
5.4	Procurement : N/A	5.14	Time & Cost Over-run : N/A
5.5	Consultancy : N/A	5.15	Project Supervision/Inspection : N/A
5.6	Contractor : N/A	5.16	Delay in Decision : N/A
5.7	Manpower : N/A	5.17	Transport : N/A
5.8	law & Order : N/A	5.18	Training : N/A
5.9	Natural calamity : N/A	5.19	Approval : N/A
5.10	Project financing, allocation and release : N/A	5.20	Others : N/A
5.11	Design formulation/approval : N/A		

6. Remarks & Recommendations of the Project Director :

It has been observed bank erosion for several years along the left bank of Padma river at Dohar Upazilla of Dhaka. A feasibility study has been conducted in 2010 by IWM to assess action plan to save live and property by implementation of protective work along the bank. According to feasibility study report it has been recommended to implement 7.5km bank Protection work from Majharchar to Moksedpur via Narisha bazar. Accordingly a project has been planed and submitted but has not been implemented due to non approval of the project. The left bank is being continued prone to erosion. The two bazar called Meghula & Narisha are severally prone to river bank erosion. The project has been taken in an emergency basis to protect these two bazar later on a technical committee was formed. After field verification the committee recommended 7.5 km implementation in this location. Accordingly a DPP has been formed based on design and estimate during estimate the value of work done has been deducted. After implementation of the temporary protection work the area has been protected from severe erosion at the left bank of Padma river for time being.

Due to implementation of the project the area is protected for the time being. To protect this area permanently a project namely "Dredging and Bank Protective Work along the Left Bank of Padma River from Majhir Char to Moksedpur via Narishabazar at Dohar Upazila under Dhaka District" with a duration upto June, 2022 has been approved by ECNEC on August 7, 2018. After implementation of permanent protective work the area will be protected from bank erosion.


Dewan Ainul Haque
Executive Engineer
Dhaka O & M Division-2
BWDB, Dhaka


(Md. Abdul Mannan Sarkar)
Superintending Engineer
Dhaka O & M Circle
BWDB, Dhaka

Date :

Signature and seal of the Project Director/Manager

7. Remarks/Comments of Agency Head

The project was prepared over night and was taken to arrest bank erosion immediately through temporary bank protective work. Dredging work has diverted the flow outwards from the bank. This project has served its purpose. It has arrested bank erosion of the project area for that time being. For permanent bank protection, a new project has been taken.

Date :


Signature and Seal
(Md. Mahfuzur Rahman)
Director General
BWDB, Dhaka.

8. Remarks/Comments of the officer in- charge of the Ministry/Division

Date :

Signature and Seal

25000-60

গণপ্রজাতন্ত্রী বাংলাদেশে স্বাধীনতা অর্জন করার জন্য যেহেতু গণতন্ত্র ছিলো :
 * নির্দিষ্ট মোতাবেক ব্যবস্থা মিলে।
 পরিকল্পনা মন্ত্রণালয়কে মর্মান্বসারে প্রতিবেদন বেশ সফল।
 * পরীক্ষা করে দেখে ফলস্বরূপ।
 পরিবীক্ষণ ও মূল্যায়ন বিভাগের আওতাধীন সর্বত্র প্রতিবেদন দিবে।
 * নির্দিষ্ট আওতাধীন সর্বত্র।
 শের-ই-বাংলা নগর, ঢাকা-১১০০।
 * নির্দিষ্ট সর্বত্র।
 www.imed.gov.bd

তারিখঃ ১১/০৭/২০১৭

[illegible]

ডায়েরী নং- ২৬৫	তারিখ- ২৫/৫/৭৭
★ তঃ বঃ (উপঃ/মহানগিরে সাক্ষাৎ) ★ বঃ পরিচালক (পিএমড) ★ বিঃ এঃ-১ ★ সিঃ বঃ (মুঃ/উপ-বিঃ এঃ/মহঃ এঃকঃ) ★ উপ-পরিচালক/সাক্ষাৎ পরিচালক ★ প্রাঃস্বঃ ★ ★	★ অতি অসহী/অসহী ★ জমোদা কলম/যজ্ঞও দিন ★ প্রতিবেদন বিঃ ★ এঃসঃসীঃ ব্যবস্থা দিন ★ পূঃসঃসঃ বিঃও দেশ কঃসঃ ★ বিঃও এঃসঃ/সঃসঃ দিন ★ ★
★ বিশিষ্ট নাক	★ প্রধান লোকেশী/কঃ অঃ

[illegible]

গ. প্রকল্পের পরিদর্শন সংক্রান্ত তথ্যঃ

১৫। প্রধান প্রধান অঙ্গের নকশা/Specification /পণ্য, কার্য ও সেবা ক্রয়ে প্রচলিত ক্রয় আইন ও বিধির অনুসরণ: ইজিপিআর মাধ্যমে ৬টি প্যাকেজ তীর সংরক্ষণ কাজের জন্য ঠিকাদার নির্বাচন করা হয়েছে। এ ক্ষেত্রে পিপিএ ২০০৬ ও পিপিআর ২০০৮ অনুসরণ করা হয়েছে।

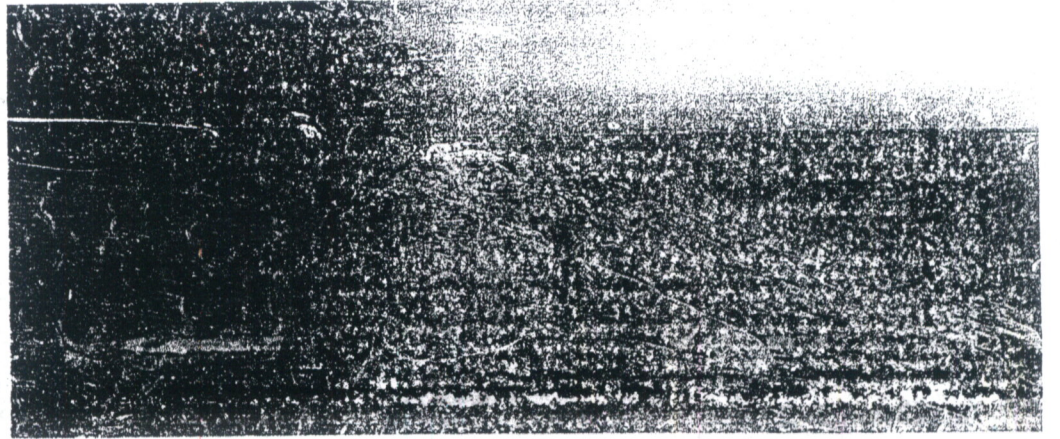
১৬। পরিদর্শনের স্থির চিত্র ও বর্ণনাঃ

১৬.১। গত ৩০/০৪/২০১৭ তারিখ প্রকল্পটি আইএমইডি'র সহকারী পরিচালক জনাব লসমী চাকমা কর্তৃক পরিদর্শন করা হয়। পরিদর্শনকালে প্রকল্প পরিচালক, বাংলাদেশ পানি উন্নয়ন বোর্ডের তত্ত্বাবধায়ক প্রকৌশলী জনাব মোঃ আব্দুল দাউদ সরকার এবং প্রকল্প সংশ্লিষ্ট অন্যান্য কর্মকর্তাগণ উপস্থিত ছিলেন।

১৬.২। পরিদর্শনে জানা যায়, ঢাকা জেলার দোহার উপজেলাধীন সরকারী প্রাথমিক বিদ্যালয়, উচ্চ বিদ্যালয়, মাদ্রাসা, মসজিদ, বসতবাড়ি, বাজার, মৎস্য ও পোলট্রি খামার, চাষযোগ্য জমি, সরকারি ও বেসরকারি স্থাপনা ইত্যাদির জন্য ১৬৮৯.৩৮ লক্ষ টাকা ব্যয়ে মে, ২০১৬ গতে জুন ২০১৭ পর্যন্ত মেয়াদে বাস্তবায়নের জন্য আলোচ্য প্রকল্পটি গ্রহণ করা হয়। প্রকল্পের কার্যক্রম ছিল চেইনেজ কি.মি. ৩.৪৮৭ থেকে কি.মি. ৪.৬৮৭ এবং কি.মি. ২.৩১২ থেকে ২.৮১২ পর্যন্ত মোট ১৭০০ মিটার অস্থায়ী প্রতিরক্ষা কাজ এবং চেইনেজ কি.মি. ২.৮১২ থেকে কি.মি. ৪.৭৩৫ পর্যন্ত ১৯২৩ মিটার নদী ড্রেজিং।

পরবর্তীতে চেইনেজ কি.মি. ২.৩১২ থেকে কি.মি. ৪.৬৮৭ এর অভ্যন্তরে ৬৭৫ মিটার এলাকায় তীর ভাঙ্গন দেখা দেয়। তা অতীতের প্রকল্পটি ১ম সংশোধন করা হয়। বার প্রশাসনিক আদেশ দ্বারা করা হয় ২৩/০২/২০১৭ তারিখে ১ম সংশোধিত ডিপিপি অনুযায়ী প্রকল্পের অনুমোদিত ব্যয় ১৯৩৪.৭৮ লক্ষ টাকা এবং বাস্তবায়নকাল মে, ২০১৬ হতে জুন ২০১৮।

১৬.৩। পরিদর্শনকালে দেখা যায়, অস্থায়ী তীর সংরক্ষণ কাজ চলমান রয়েছে। প্রকল্প পরিচালক জানান, আলোচ্য প্রকল্পে মোট ৬টি প্যাকেজের আওতায় কাজ করা হচ্ছে। এর মধ্যে ৫টি অস্থায়ী তীর সংরক্ষণ কাজ এবং অন্যটি নদী ড্রেজিং। ডিপিপি ডিজাইন অনুযায়ী নদী তীর হতে ৩০ মিটার লক্ষিং এপ্রোনে অস্থায়ী তীর প্রতিরক্ষা কাজ করা হচ্ছে। প্রকল্প পরিচালক জানান, অস্থায়ী প্রতিরক্ষা কাজে ২৫০ কেজি ওজনের বালু ভর্তি জিও ব্যাগ ও গুনি ব্যাগ ব্যবহার করা হচ্ছে। পরিদর্শনকালে র‍্যানডম সিলেকশনের মাধ্যমে কিছু জিও ব্যাগ পরিমাপ করা হয় এবং নির্দিষ্ট পরিমাণ ওজন (২৫০ কেজি এবং কিছু ২৫০ কেজি ওর্ধে) পাওয়া যায় (চিত্র-১)। প্রকল্পের পরিচালক জানান, ১৭০০ মিটার অংশে জিও ব্যাগ ভাঙ্গি-প্রায় সম্পন্ন করা হয়েছে। বর্তমানে জিও ব্যাগ প্রেসিং করা হচ্ছে। ডিপিপি ডিজাইন অনুযায়ী ২০০ কেজি ওজনের ২০টি করে জিও ব্যাগ ২ লেয়ারে প্রেসিং করা হচ্ছে (চিত্র-২)।



চিত্র-১: পরিমাপকৃত জিও ব্যাগ

১৭। পর্যবেক্ষণঃ

১৭.১ আলোচ্য প্রকল্পটির কার্যক্রম ডিপিপি'র কর্মসূচিকল্পনার সাথে সামঞ্জস্যপূর্ণ। জুন, ২০১৭ পর্যন্ত এ প্রকল্পের বাস্তব অগ্রগতি ৮৬.৩৭%। অবশিষ্ট ১৩.৬৩% কাজ নির্ধারিত সময় জুন, ২০১৮ তে সমাপ্ত করা সম্ভবপর হবে বলে প্রতীয়মান হয় এবং

১৭.২ প্রকল্পের কার্যক্রম দ্রুতগতিতে এগিয়ে চলছে, তবে কাজের গুণগতমান বজায় রাখতে মাঠ পর্যায়ে আরো জোর মনিটরিং প্রয়োজন।

১৮। সুবিধাবোগীর মতামতঃ প্রকল্পটি বাস্তবায়নের ফলে বাজার, বসত বাড়িসহ অফিসসমূহ সংরক্ষণ করা সম্ভব হবে জানিয়ে স্থানীয় অধিবাসীগণ তীর প্রতিরক্ষা বিষয়ে সন্তোষ প্রকাশ করেন।

୧୯। ମୁଖାବିଶଃ

১৯.১ প্রকল্পের কাজ সুষ্ঠুভাবে সম্পাদন এবং গুণগত মান রক্ষার্থে মহানগর এবং হাট পর্যায়ে প্রকল্প সংশ্লিষ্ট কর্মকর্তাদের মনিটরিং জোরদার করতে হবে;

১৯.২ প্রকল্পটি ইতোমধ্যে ১ম বার সংশোধন করে প্রকল্পের মেয়াদ ১ বছর বৃদ্ধি করা হয়েছে। কাজেই বর্তমানে নির্ধারিত সময়ে জন, ২০১৮ তে প্রকল্প সমাপ্তির বিষয়ে সচেষ্ট থাকতে হবে এবং এ ক্ষেত্রে প্রয়োজনীয় পদক্ষেপ গ্রহণ করতে হবে।

১৯.৩ অনুচ্ছেদ ১৯.১ - ১৯.২ পর্যন্ত সুপারিশের আলোকে গৃহীত ব্যবস্থা আগামী ১(এক) মাসের মধ্যে আইএমইডিতে অবহিত করতে হবে।

১৯৬৭. ২০০৬
পরিদর্শনকারী কর্মসূচী
ফোন নম্বর ১৯৬৭. ২০০৬
সহকারী পরিদর্শক
পরিদর্শনকারী কর্মসূচী

তারিখঃ ২৭ জ্যৈষ্ঠ, ১৪২৫
১০ জুন, ২০১৮

বিষয় : “ঢাকা জেলার দোহার উপজেলাধীন পশ্চিম নারিনা বাজার এবং মেঘুলা বাজার সংলগ্ন পদ্মা নদীর বামতীরে অস্থায়ী প্রতিরক্ষামূলক কাজ” শীর্ষক প্রকল্পের পরিদর্শন প্রতিবেদন প্রসঙ্গে।

উপর্যুক্ত বিবরণ ও সূত্রের বরাতে জানানো যাচ্ছে যে, বিষয়োক্ত প্রকল্পটি গত ২৪-০৫-২০১৭ তারিখে আইএসইডি কর্তৃক পরিদর্শিত হয়। উক্ত পরিদর্শন প্রতিবেদনের সুপারিশ/মতামতের আলোকে পরবর্তী প্রয়োজনীয় ব্যবস্থা গ্রহণের নিমিত্ত পরিদর্শন প্রতিবেদনের ছায়ািলিপি এতদসঙ্গে সংযুক্ত করে নির্দেশক্রমে প্রেরণ করা হলো।

সংযুক্তিঃ সূত্রোহ পত্রের অনুলিপি ।

2000

মুহাম্মদ মাজহারুল ইসলাম চৌধুরী

মহাকবি প্রবাল

தேதி : 20/09/2022

মহাপরিচালক
বাংলাদেশ পানি উন্নয়ন বোর্ড
ওয়াশাডা ভবন
মতিঝিল বা/এ, ঢাকা।
(দৃঃআঃ প্রধান, পরিকল্পনা)

অনুলিপিঃ

১। তত্ত্বাবধায়ক প্রকৌশলী, ঢাকা পওর সার্কেল, বাংলাদেশ পানি উন্নয়ন বোর্ড, ঢাকা।
২। উপ-প্রধান ১ মহোদয়ের ব্যক্তিগত কর্তৃকর্তা, পানি সম্পদ মন্ত্রণালয়, বাংলাদেশ সচিবালয়, ঢাকা।
৩। সংশ্লিষ্ট/মাষ্টার নথি।

ডায়েরী নং-	তারিখ-১৩/০৫/১৮
* যুগ্ম প্রধান	* জরুরী
* অধ্যক্ষ প্রমোদীশালী	* কাকোচনা করণ
* পরিচালক ১/২/৩ প্রমোদ	* ব্যবস্থা নিব
* নির্বাহী প্রমোদীশালী/২/৩	* নথিতে রাখ
* জিবি (প্রমোদ)	* আহিনপ্রমোদ
* উপ প্রধান (কৃষি/পরিবেশ)	* উপপ্রমোদ করণ
* শিএ	

১৮/০৫/১৮

১. প্রাথমিক শিক্ষা	১০০	১০০
২. মাধ্যমিক শিক্ষা	১০০	১০০
৩. উচ্চ মাধ্যমিক শিক্ষা	১০০	১০০
৪. বিশ্ববিদ্যালয়	১০০	১০০
৫. গবেষণা	১০০	১০০
৬. প্রশিক্ষণ	১০০	১০০
৭. প্রশাসন	১০০	১০০
৮. অর্থ	১০০	১০০
৯. স্বাস্থ্য	১০০	১০০
১০. পরিবার কল্যাণ	১০০	১০০
১১. শ্রম	১০০	১০০
১২. কৃষি	১০০	১০০
১৩. মৎস্য	১০০	১০০
১৪. পশুপালন	১০০	১০০
১৫. খনিজ	১০০	১০০
১৬. শিল্প	১০০	১০০
১৭. পরিবহন	১০০	১০০
১৮. যোগাযোগ	১০০	১০০
১৯. বিদ্যুৎ	১০০	১০০
২০. জল	১০০	১০০
২১. আবহাওয়া	১০০	১০০
২২. পরিবেশ	১০০	১০০
২৩. নগরায়ণ	১০০	১০০
২৪. স্থানীয় সরকার	১০০	১০০
২৫. জনসংস্কৃতি	১০০	১০০
২৬. ভাষা	১০০	১০০
২৭. সাহিত্য	১০০	১০০
২৮. শিল্পকলা	১০০	১০০
২৯. সঙ্গীত	১০০	১০০
৩০. খেলা	১০০	১০০
৩১. স্পোর্টস	১০০	১০০
৩২. ভ্রমণ	১০০	১০০
৩৩. পরিদর্শন	১০০	১০০
৩৪. প্রশিক্ষণ	১০০	১০০
৩৫. প্রশাসন	১০০	১০০
৩৬. অর্থ	১০০	১০০
৩৭. স্বাস্থ্য	১০০	১০০
৩৮. পরিবার কল্যাণ	১০০	১০০
৩৯. শ্রম	১০০	১০০
৪০. কৃষি	১০০	১০০
৪১. মৎস্য	১০০	১০০
৪২. পশুপালন	১০০	১০০
৪৩. খনিজ	১০০	১০০
৪৪. শিল্প	১০০	১০০
৪৫. পরিবহন	১০০	১০০
৪৬. যোগাযোগ	১০০	১০০
৪৭. বিদ্যুৎ	১০০	১০০
৪৮. জল	১০০	১০০
৪৯. আবহাওয়া	১০০	১০০
৫০. পরিবেশ	১০০	১০০
৫১. নগরায়ণ	১০০	১০০
৫২. স্থানীয় সরকার	১০০	১০০
৫৩. জনসংস্কৃতি	১০০	১০০
৫৪. ভাষা	১০০	১০০
৫৫. সাহিত্য	১০০	১০০
৫৬. শিল্পকলা	১০০	১০০
৫৭. সঙ্গীত	১০০	১০০
৫৮. খেলা	১০০	১০০
৫৯. স্পোর্টস	১০০	১০০
৬০. ভ্রমণ	১০০	১০০
৬১. পরিদর্শন	১০০	১০০
৬২. প্রশিক্ষণ	১০০	১০০
৬৩. প্রশাসন	১০০	১০০
৬৪. অর্থ	১০০	১০০
৬৫. স্বাস্থ্য	১০০	১০০
৬৬. পরিবার কল্যাণ	১০০	১০০
৬৭. শ্রম	১০০	১০০
৬৮. কৃষি	১০০	১০০
৬৯. মৎস্য	১০০	১০০
৭০. পশুপালন	১০০	১০০
৭১. খনিজ	১০০	১০০
৭২. শিল্প	১০০	১০০
৭৩. পরিবহন	১০০	১০০
৭৪. যোগাযোগ	১০০	১০০
৭৫. বিদ্যুৎ	১০০	১০০
৭৬. জল	১০০	১০০
৭৭. আবহাওয়া	১০০	১০০
৭৮. পরিবেশ	১০০	১০০
৭৯. নগরায়ণ	১০০	১০০
৮০. স্থানীয় সরকার	১০০	১০০
৮১. জনসংস্কৃতি	১০০	১০০
৮২. ভাষা	১০০	১০০
৮৩. সাহিত্য	১০০	১০০
৮৪. শিল্পকলা	১০০	১০০
৮৫. সঙ্গীত	১০০	১০০
৮৬. খেলা	১০০	১০০
৮৭. স্পোর্টস	১০০	১০০
৮৮. ভ্রমণ	১০০	১০০
৮৯. পরিদর্শন	১০০	১০০

[illegible]

১০. (ক) ডিপিপি/আরডিপি'তে মোট প্যাকেজ সংখ্যা: প্রকল্পটির মোট প্যাকেজ সংখ্যা: ৩৭টি।

(খ) পণ্য, কার্য ও সেবা ক্রয় সংক্রান্ত তথ্য: প্রকল্প পরিচালক হতে প্রাপ্ত চলতি অর্থ বছরে চ্যামনি প্যাকেজের কার্যের বর্ণনা নিম্নে দেয়া হলো:

প্যাকেজ নং.	দরপত্র আহ্বানের তারিখ ও প্রারম্ভিত মূল্য	চুক্তির তারিখ ও চুক্তি মূল্য	কাজ সমাপ্তির তারিখ		কাজের বর্ণনা
			চুক্তি অনুযায়ী	প্রকৃত	
e-Tender/OTM / Narisha/TBP-01 / 2015-16	16-06-2016 27637349.970	16-08-2016 23491525.641	15-01-2017	31-05-2017	নির্দেশনা অনুযায়ী (বাধা) পেমেন্ট/কম্পেন্সি পেমেন্ট
e-Tender/OTM / Narisha/TBP-02 / 2015-16	13/06/2016 27637305.860	16-08-2016 23491525.641	15-01-2017	31-05-2017	ইউনিয়নের বা পাওয়ার লাইন চুক্তি অনুযায়ী
e-Tender/OTM / Narisha/TBP-03 / 2015-16	13/06/2016 27637305.860	10-08-2016 25910850.448	08-01-2017	31-05-2017	অগ্রগতিতে কাজের বর্ণনা সমাপ্ত হওয়া
e-Tender/OTM / Meghula/TBP-04 / 2015-16	13/06/2016 17273349.250	16-08-2016 15546014.326	15-01-2017	31-05-2017	জল সরবরাহের সুবিধা
e-Tender/OTM / Meghula/TBP-05 / 2015-16	01/08/2016 17273349.250	27-09-2016 15546014.326	29-05-2017	31-05-2017	
e-Tender/OTM / Narisha/TBP-06 / 2015-17	29-03-2017 44038585.810	30-04-2017 39631727.286	30-05-2017	31-05-2017	জল সরবরাহের সুবিধা
Dredging-07	49967232.00	31-07-2016 49967232.00	30-05-2017	30-06-2017	নদীর তট পরিষ্কার

১১। প্রকল্প পরিচালক সম্পর্কিত তথ্য (পর্যায়ক্রমে প্রকল্প শুরু হতে বর্তমান সময় পর্যন্ত):

প্রকল্প পরিচালক-এর আইডি নং	মূল দায়িত্ব ও পদাবি	পদোন্নতি	দায়িত্বের সময় (দিন/মাস/বছর)	অন্যান্য তথ্য
মোঃ আব্দুল মতিন সরকার ৬৪০১০৫০০২	তত্ত্বাবধায়ক প্রকৌশলী, ঢাকা পওর সার্কেল, বাপাউবো, ঢাকা	০১/০১/২০১৬ হতে বর্তমান	অতিরিক্ত	

১২। ভূমি অধিগ্রহণ: ভূমি অধিগ্রহণের কোন প্রতিশ্রুতি ছিল না।

১৩। অডিট সম্পাদন ও আগতি নিষ্পত্তি সংক্রান্ত তথ্য: ২০১৬-২০১৭ অর্থ বছর পর্যন্ত সরকারি পূর্ত অডিট সম্পন্ন হওয়ায় অত্র প্রকল্পের অনুকূলে কোন অডিট আপত্তি নাই।

১৪। স্টিয়ারিং/পিআইসি সভা সংক্রান্ত: প্রকল্পটির ১ম সভা গত ২৭-০৬-২০১৭ খ্রিঃ এবং ২য় সভা গত ১০-০৭-২০১৭ খ্রিঃ তারিখে পানি সম্পদ মন্ত্রণালয়ের সিনিয়র সচিব মহোদয়ের সভাপতিত্বে অনুষ্ঠিত হয়।

কমিটির সিদ্ধান্ত	নির্দেশনা প্রতিপালন
(ক) প্রকল্পের অবশিষ্ট কাজ নির্ধারিত স্বেচ্ছায় জুন/২০১৮ এর মধ্যে সমাপ্ত করতে হবে;	প্রকল্পের অবশিষ্ট কাজের সমাপ্তি
(খ) প্রকল্প সমাপ্তির পর যথানিয়মে প্রকল্প সমাপ্ত মূল্যায়ন (PCR) দাখিল করতে হবে।	প্রকল্প পরিচালক আসনসে যে ডিআইসি সভা সমাপ্তির পর প্রকল্পের সমাপ্তি মূল্যায়ন (PCR) দাখিল করতে হবে।

১৫। নদীর গভীরতা এবং বর্ষা মৌসুমে পদ্মা নদীর পানির তীব্রতা বিবেচনায় এপ্রিল-মে/২০১৭ তে শুধু ২ (দুই) স্তরের জিও ব্যাগ দ্বারা ১৬ ঘন মিটার/মিটার ডিজাইনে ডাম্পিং কাজ করে অস্থায়ী প্রতিরক্ষা কাজ করার পরও অদ্যাবধি কেন স্থায়ী প্রতিরক্ষা কার্যক্রম গ্রহণ করা হলো না জিজ্ঞাসা করা হলে প্রকল্প পরিচালক জানান যে অস্থায়ীভাবে তীর প্রতিরক্ষার প্রকল্প বাস্তবায়ন কালেই প্রকল্প এলাকার নদীর অবস্থা বিবেচনা করে স্থায়ী প্রতিরক্ষা কাজের জন্য একটি প্রকল্প প্রণয়ন কাজ শুরু করা হয়েছিল। কারিগরি কমিটির রিপোর্ট নিয়ে প্রকল্প এলাকার “মাকিরচর হতে নারিশা বাজার হয়ে মোকসেদপুর পর্যন্ত ৭.৫০ কি:মি: স্থায়ী নদী তীর সংরক্ষণমূলক কাজ” শীর্ষক প্রকল্প প্রণয়ন করা হয়। প্রকল্পটি মন্ত্রণালয় হয়ে পরিকল্পনা কমিশনে আসে। গত ১৪/০২/২০১৮ তারিখে প্রকল্পের পিইসি সভাও অনুষ্ঠিত হয়েছে। কিন্তু প্রকল্পটি একনেক সভায় এখনো যায়নি।

ক.৬। প্রকল্পটির ২৩৭৫ মিটার প্রতিরক্ষা কাজের এলাকাসহ এর উজানে এবং ভাটিতে নদী তীরের যে ভাংগণ প্রবণতা পরিদর্শনকালে লক্ষ্য করা গেছে তাতে এবারের বর্ষা মৌসুমে সম্পাদিত ২৩৭৫ মিটার অস্থায়ী প্রতিরক্ষা কাজের প্রায় সবটুকুই নদী গর্ভে বিলীন হয়ে যাওয়ার সমূহ আশংকা রয়েছে।

ক.৭। পরিদর্শনকালে দেখা যায় সম্পাদিত কাজ রক্ষাকল্পে নদীতীরে যেখানে ফাটল দেখা দিয়েছে এবং পাশবর্তী এলাকার বৃষ্টির পানি নামার কারণে ধসে যাওয়ার উপক্রম হয়েছে। সেখানে বালির বস্তা দিয়ে তা প্রতিরোধ করার চেষ্টা চলছে দেখা গেল।

ক.৮। পরিদর্শনকালে প্রকল্প পরিচালক জানান যে, ডিপিরি'র সংস্থান মোতাবেক অক্ষাংশ-দ্রাঘিমাংশ ঠিক করে ১৯২০ মিটার ড্রেজিং কাজ সম্পন্ন করা হয়েছে।

খ. পণ্য, কার্য ও সেবা ত্রয় প্রচলিত আইন/বিধি অনুসরণ: প্রকল্পটির আওতায় ড্রেজিং কার্যক্রম ছাড়া অন্য ৬ (ছয়)টি প্যাকেজের কাজ ই-টেন্ডারের মাধ্যমে সম্পন্ন হয়েছে মর্মে জানা যায়।

গ. সাইট বই পর্যালোচনা (ভৌত কাজের ক্ষেত্রে): সাইট পরিদর্শনকালে কার্য সাইটে পরিদর্শন বই সংরক্ষণ করা হচ্ছে দেখা গিয়েছে। কর্মকর্তাগণ সাইট পরিদর্শনকালে ঠিকাদারগণকে কাজের মান নিয়ন্ত্রণ, অগ্রগতি, পদ্ধতি, ইত্যাদি বিষয়ে নির্দেশনা প্রদান করেছেন মর্মে দেখা গেল।

ঘ. সুবিধাভোগীদের মতামত: পরিদর্শন কালে প্রকল্প এলাকার জনগণের সুবিধাদির বিষয়ে কয়েক জনের সাথে আলোচনা করা হয়। তারা জানান যে, প্রকল্পটির কার্যক্রম বাস্তবায়নের ফলে ২০১৬ সাল থেকে ভাংগণ কিছুটা রোধ হয়েছে কিন্তু এবার তারা খুব শংকায় আছেন। তাদের অনেক উপকার হয়েছে। তবে স্থায়ী প্রতিরক্ষা কাজ দ্রুত বাস্তবায়নের জন্য প্রকল্প এলাকার জনগণ জোরালো দাবী জানান।

১৮। সার্বিক পর্যবেক্ষণঃ

১৮.১। আইএমইডি'র সহকারী পরিচালক জনাব লসমী চাকমা কর্তৃক পরিদর্শন প্রতিবেদন যা ১১/০৭/২০১৭ তারিখে প্রেরণ করা হয়েছে (অনুচ্ছেদ ১৬.খ) সেটির পরিপালন প্রতিবেদন প্রেরণ না করা বা গৃহীত ব্যবস্থাদি সম্পর্কে আইএমইডিকে অবহিত না করার বিষয়টি অপ্রত্যাশিত;

১৮.২। প্রকল্প এলাকায় গভীরতা ও ভাংগণ প্রবণতা বিবেচনায় ১৬ ঘন মিটার/মিটার ডিজাইনে শুধু জিও ব্যাগ ডাম্পিং এবং প্রেসিং করে অস্থায়ী প্রতিরক্ষা কাজ করার প্রায় ২ (দুই) বৎসরের মধ্যেও স্থায়ী প্রতিরক্ষা কাজ বাস্তবায়ন কার্যক্রম শুরু না করা সুবিবেচনার কাজ হয়নি;


১৮.৩। অস্থায়ী তীর প্রতিরক্ষা কাজের জন্য ব্যয়কৃত অর্থ খরচ একেবারে বিফলে যাবে যদি অনতিবিলম্বে/এখনই স্থায়ী প্রতিরক্ষা কার্যক্রম শুরু করা না হয়। কারণ এ বছর বাস্তবায়িত কাজ টিকবে কিনা সে বিষয়ে যথেষ্ট সন্দেহ রয়েছে;

১৮.৪। ২৩৭৫ মিটার বাস্তবায়িত অস্থায়ী তীর প্রতিরক্ষা কাজ রক্ষাকল্পের দ্রুত স্থায়ী তীর প্রতিরক্ষা কাজের জন্য প্রস্তাবিত প্রকল্পটি বাস্তবায়ন কার্যক্রম এখনই শুরু করে এলাকাবাসীর স্থাবর-অস্থাবর সম্পত্তিসহ বিভিন্ন স্থাপনা রক্ষার জরুরী উদ্যোগ গ্রহণ করে এলাকাবাসীর দু:শ্রিত্তা লাঘব করা একান্ত প্রয়োজন;

১৮.৫। প্রকল্পের আওতায় ৬ (ছয়)টি প্যাকেজে ২৩৭৫ মিটার অস্থায়ী তীর প্রতিরক্ষার কাজ সম্পন্ন হয়েছে অর্থাৎ বাস্তব কাজের অগ্রগতি ১০০% এবং আর্থিক অগ্রগতি ১৫৬৬.২২ লক্ষ টাকা (৭৯.৯৩%);

২০। সুপারিশ/মতামতঃ

- ২০.১। আইএমইডি'র সহকারী পরিচালক জনাব লসমী চাকমা কর্তৃক পরিদর্শন প্রতিবেদনের (অনুচ্ছেদ ১৬.খ) আলোকে গৃহীত ব্যবস্থাদি পরিপালন প্রতিবেদন আইএমইডিতে প্রেরণ করতে হবে (অনুচ্ছেদ ১৮.১);
- ২০.২। প্রকল্পের আওতায় সম্পাদিত ২৩৭৫ মিটার অস্থায়ী তীর প্রতিরক্ষা কাজ ঠিকিগে রাখাসহ ইতোমধ্যে ব্যয়কৃত সরকারী অর্থের সঠিক ব্যবহার নিশ্চিত করতে এখনই “মাঝিরচর হতে নারিশা বাজার হয়ে মোকসেদপুর পর্যন্ত ৭.৫০ কি:মি: স্থায়ী নদী তীর সংরক্ষণমূলক কাজ” শীর্ষক প্রস্তাবিত প্রকল্পটির বাস্তবায়ন করার বিষয়ে সংশ্লিষ্ট মন্ত্রণালয়/সংস্থা জরুরী ও কার্যকরী উদ্যোগ গ্রহণ করতে হবে (অনুচ্ছেদ ১৭.ক.৫ ও ১৮.৪);
- ২০.৩। বর্তমানে এলাকাটি যেহেতু খুবই ভাংগন প্রবণতা দেখা দিয়েছে সেহেতু অস্থায়ী প্রতিরক্ষা কাজ রক্ষার প্রচেষ্টা অব্যাহত রাখতে হবে (অনুচ্ছেদ ১৭.ক.৭);
- ২০.৪। চলমান প্রকল্পটির কাজ যেহেতু ইতোমধ্যে ১০০% সমাপ্ত হয়েছে তাই বিলম্ব না করে যথানিয়েমে পিসিআর দাখিল করতে হবে;
- ২০.৫। পরিদর্শন প্রতিবেদনের উপর গৃহীত ব্যবস্থাবলী আগামী ১ (এক) মাসের মধ্যে আইএমইডিকে অবহিত করতে হবে।


(মোঃ আশফুর রহমান)
পরিচালক (উপসচিব)
